




TECHNICAL PROPOSAL



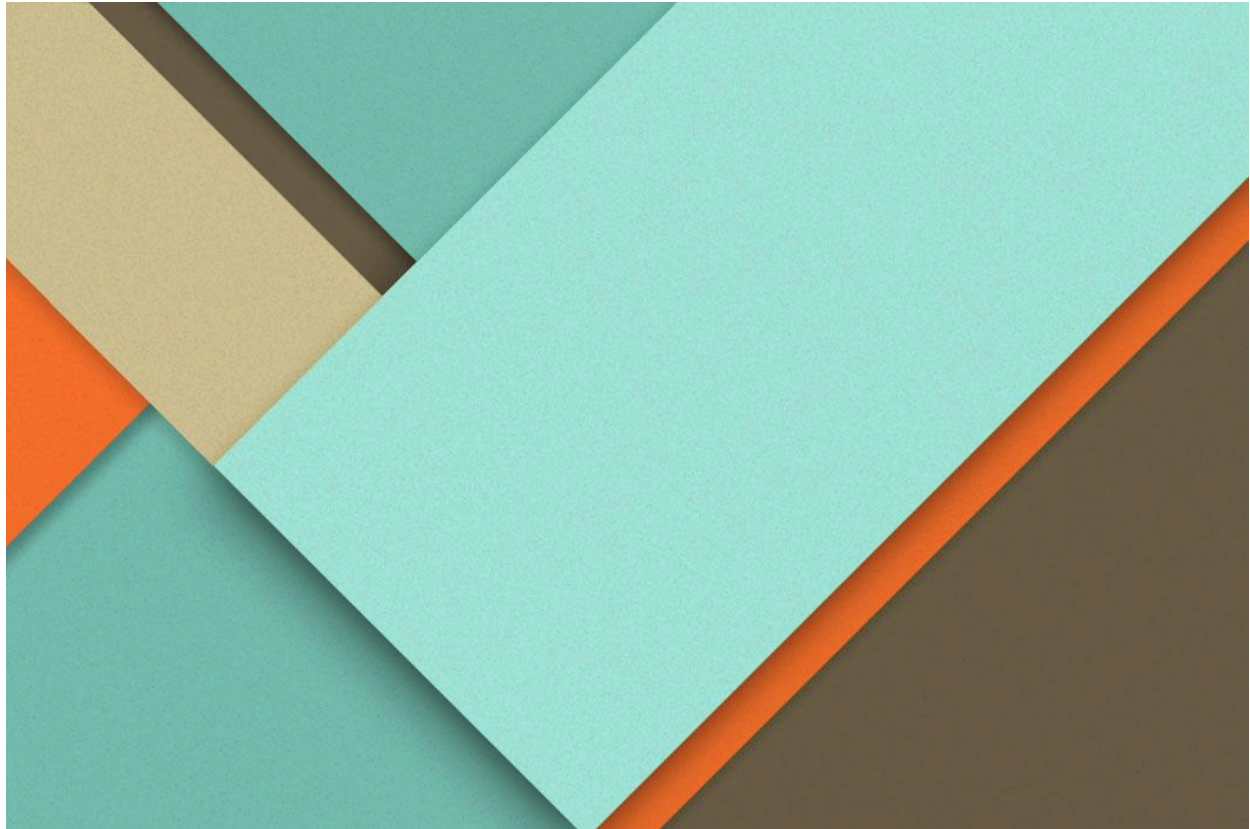

**REPUBLIC OF KENYA
COUNTY GOVERNMENT OF ISIOLO
DEPARTMENT OF REVENUE**



TECHNICAL PROPOSAL

**REVENUE AUTOMATION SYSTEM FOR COUNTY GOVERNMENT OF
ISIOLO
TENDER NO: CGI/RFP/ FEP/01/2025-2026**

SUBMITTED BY:

HYDROLIFE TECH LIMITED

9TH FLOOR, CIANDA HOUSE, NAIROBI

P.O. BOX 37646 - 00100,

NAIROBI-KENYA.

TEL: 0731206395

EMAIL: info@hydrolifetech.com

NOV, 2025

Table of Contents

1. Technical proposal submission form.....	1
2. Company profile.....	2
2. Firms references	
3. Comments and suggestions of consultants on the Terms of reference and on data.....	3
services and facilities to be provided by the procuring entity.....	4
4. Description of the methodology and work plan for performing the assignment.....	5
5. Team composition and Task assignments.....	6
6. Format of curriculum vitae (CV) for proposed Professional staff.....	7
7. Time schedule for professional personnel.....	8
8. Activity (work schedule).....	9
9. Knowledge Transfer and Capacity Building plan.....	10

TECHNICAL PROPOSAL SUBMISSION FORM

[23rd Nov 2025]

**To: THE CHIEF OFFICER REVENUE COUNTY
GOVERNMENT OF ISIOLO P.O BOX 36 60300 ISIOLO**

Ladies/Gentlemen:

We, the undersigned, offer to provide the consulting services for the project titled:

REVENUE AUTOMATION SYSTEM FOR COUNTY GOVERNMENT OF ISIOLO

TENDER NO: CGI/RFP/ FEP/01/2025-2026

in accordance with your Request for Proposal dated **12th Nov 2025** and our Proposal.

We are hereby submitting our Proposal, which includes this Technical Proposal.

Members of the project team include the following key service areas:

Service Area	Authorized Signature
(i) Software Development Services	Chege Danche Ng'ang'a
(ii) Systems Analysis & Design	Mathews Onyango Ong'any
(iii) Database & Infrastructure Services	Calvin Njuguna Ngugi
(iv) Cybersecurity & Quality Assurance Services	Joel Ngite Mutisya

We understand you are not bound to accept any Proposal that you receive.

We remain,


Yours sincerely,

_____ **[Authorized Signature]**

_____ **[Name and Title of Signatory]**

_____ **[Name of Firm]**

_____ **[Address]**

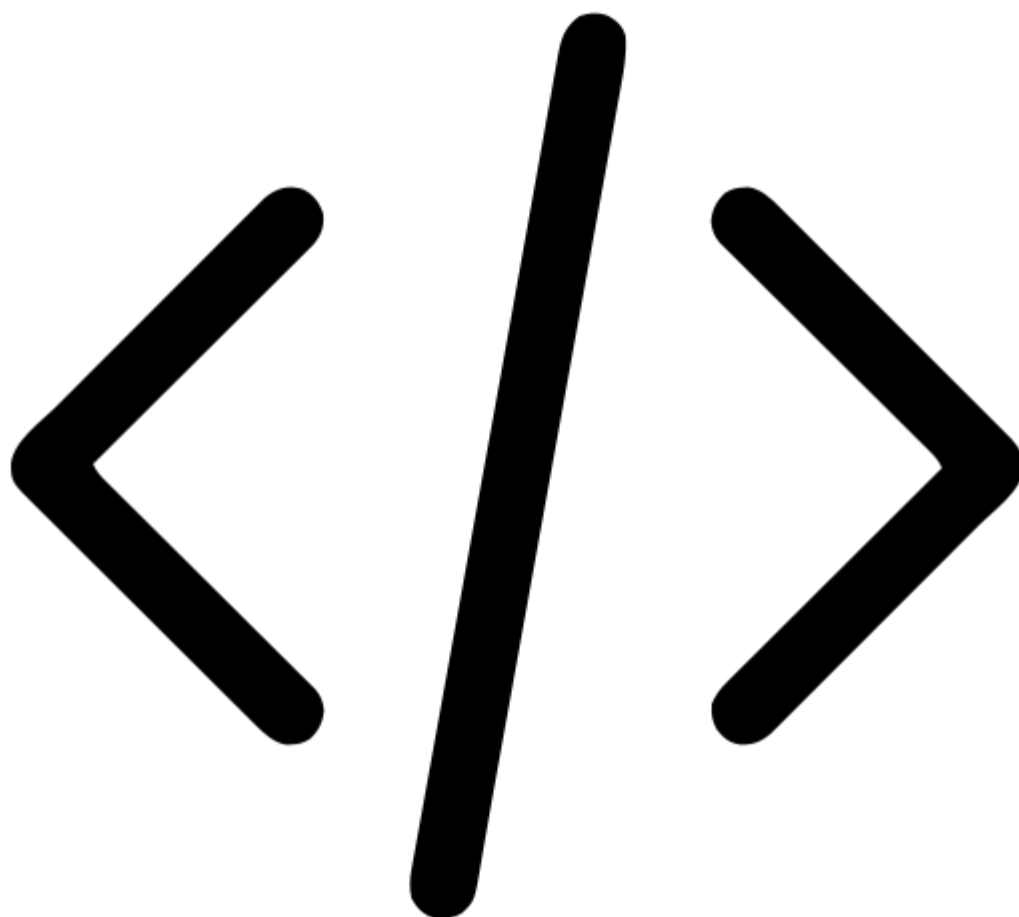

HYDROLIFE TECH

COMPANY PROFILE

HYDROLIFE TECH LIMITED

1. Company Summary

Company Name: **Hydrolife Tech Limited**

Type: Software Engineering Firm / Digital Solutions Provider

Head Office: 9th Floor, Cianda Hse, Nairobi, Kenya.

Email: info@hydrolifetech.com

Website: <https://www.hydrolifetech.com>

Director: Kulah Jirma

Director Email: kulah@hydrolifetech.com

Director Phone: +254 731 206 395

Hydrolife Tech is a professional Kenyan software engineering company that designs, builds, and maintains modern digital solutions for businesses, government entities, and startups. We combine software engineering best practices with product-minded thinking to deliver sustainable, scalable, and high-impact systems.

2. Mission, Vision & Values

Mission

To empower organizations to achieve digital transformation through well-engineered, user-focused software solutions that solve real business problems and create lasting value.

Vision

To be a leading and trusted technology partner across East Africa and beyond, recognized internationally for technical excellence, reliability, and measurable business impact.

Core Values

- **Innovation:** Continuously adopt and apply modern technologies to deliver novel and efficient solutions that keep our clients competitive.
- **Quality:** Maintain a strong emphasis on clean architecture, comprehensive testing, robust security, and long-term maintainability across all projects.
- **Collaboration:** Foster transparent and integrated partnerships with clients, acting as a dedicated and professional extension of their internal team.
- **Integrity:** Ensure honest communication, predictable, on-time delivery, and the

highest ethical standards in all business practices.

- **Customer Success:** We fundamentally measure our success by the tangible business outcomes and growth our clients achieve through our solutions.

3. Capabilities & Services

Hydrolife Tech offers a comprehensive suite of digital services covering the entire product lifecycle:

End-to-end Software Delivery

- Requirements discovery, user-centric product design, and rapid prototyping.
- Architecture & systems design (specializing in cloud-native, microservices, and optimized monoliths where appropriate).
- Implementation of robust web applications, mobile apps, scalable APIs, and reliable backend systems.
- Quality assurance, automated testing (unit, integration, end-to-end), and performance tuning to ensure stability under load.

Cloud & Infrastructure

- Expert cloud architecture and deployment on major cloud providers (AWS, Azure, and others).
- Containerization and orchestration using industry standards like Docker and Kubernetes.
- Implementation of automated CI/CD pipelines, comprehensive monitoring, logging, and full DevOps practices.

Data & Integration

- Professional API design and seamless integrations with third-party systems, including payment gateways, SMS/email providers, and external enterprise platforms.
- Data modelling, robust ETL (Extract, Transform, Load) pipelines, and creation of basic analytics/dashboards for business insights.

Maintenance & Support

- SLA-based support tailored to client needs, ensuring rapid bug-fixing, secure version upgrades, and continuous functional improvements.

Digital Transformation & Consulting

- Strategic process automation, comprehensive system modernization, legacy migration, and objective vendor evaluation.

UX / UI

- In-depth user research, detailed wireframes, compelling visual design, and professional front-end development to ensure highly usable and accessible products.

4. Technology & Methodology

Hydrolife Tech utilizes modern, maintainable, and scalable technology stacks:

Technologies (Representative Stack)

- **Backend:** Node.js, Golang, Python (Django/Flask), Java / Spring Boot (selected based on project requirements and performance needs).
- **Frontend:** React, Vue, and similar Single Page Application (SPA) frameworks.
- **Mobile:** React Native / Flutter (for cross-platform efficiency) or native development where complex hardware integration is required.
- **Databases:** PostgreSQL, MySQL, and various NoSQL options (e.g., MongoDB) for diverse data needs.
- **DevOps:** Docker, Kubernetes, CI/CD (GitHub Actions, GitLab CI, Jenkins), and Infrastructure as Code principles.

Delivery Approach

- **Agile:** We follow Agile methodologies (Scrum/Kanban) with iterative deliveries, continuous client feedback loops, and regular software demos.
- **Quality First:** We employ a test-driven mindset with extensive automated tests, mandatory code reviews, and clean architectural principles.
- **Security:** Development is security-conscious, implementing basic compliance controls, robust role-based access systems, and secure credentials handling.

5. Typical Projects & Use Cases

Hydrolife Tech has a proven track record delivering essential digital products across various sectors:

- **SaaS Platforms:** Building complete Software-as-a-Service platforms for Small to Medium Enterprises (SMEs) and large enterprises, enabling subscription-based

revenue models.

- **Custom Portals:** Developing tailored web portals and comprehensive client management systems (CMS) for internal operations and external client interaction.
- **Mobile Solutions:** Creating mobile applications for streamlined field operations, remote data collection, and enhanced customer engagement.
- **Integration Services:** Implementing complex integrations with payment processors, SMS/mapping services, and logistics platforms to automate and streamline service delivery chains.
- **Digitization:** Executing the complete digitization of manual, paper-based processes for government agencies and non-governmental organizations (NGOs) to improve efficiency and transparency.

6. Team & Leadership

Director: Kulah Jirma — Principal decision-maker, strategic lead, and primary client contact. (kulah@hydrolifetech.com, +254 731 206 395)

Technical Teams: Our workforce comprises cross-functional experts including highly skilled backend, frontend, and mobile engineers, dedicated QA/test engineers, DevOps/generalists, and experienced UX/UI practitioners.

Engagement Model: We offer flexible engagement models, including project-based teams for defined scopes and extended-team models (dedicated engineers) for ongoing development partnerships.

7. Accreditation & Trust Signals

ICT Authority Accreditation: Hydrolife Tech is an officially Accredited Supplier, listed on the Kenya ICT Authority's register. This accreditation supports eligibility for government procurement and assures our capacity for public-sector projects.

Public Presence: We maintain a comprehensive public website detailing our services, technical approach, and contact channels, ensuring full transparency.

8. Quality, Security & Compliance

Hydrolife Tech prioritizes technical excellence and operational security through strict adherence to industry best practices:

- **Code Quality:** Enforced through code linters, automated style checks, and rigorous peer

code reviews.

- **Automated Testing:** Implementation of a multi-tiered testing strategy including unit, integration, and security tests.
- **Security:** Secure handling of all sensitive credentials and production secrets using dedicated vaults and established security protocols.
- **Business Continuity:** Comprehensive backup and recovery plans are implemented for all hosted solutions, leveraging robust cloud provider features to guarantee resilience.
- **Maintenance & Response:** Formal Service Level Agreements (SLAs) are established for maintenance and incident response, guaranteeing rapid resolution times customized to each client's critical needs.

9. Example Client Engagement Process

Our proven, structured engagement process ensures clarity, quality, and consistent delivery:

1. **Discovery & Proposal:** Detailed gathering of requirements, mapping of current business flows, followed by the production of a clear scope of work and a fixed or estimated cost proposal.
2. **Design & Roadmap:** Creation of UX wireframes, definition of the optimal system architecture, and setting clear, achievable project milestones.
3. **Development Iterations:** Execution of work in short sprint cycles, featuring regular demos and continuous client feedback integration.
4. **Testing & Hardening:** Rigorous user acceptance testing (UAT), comprehensive security checks, and performance tuning to ensure production readiness.
5. **Deploy & Handover:** Successful production launch, full system training for client teams, and detailed technical documentation.
6. **Support & Evolution:** Provision of ongoing maintenance, operational support, and strategic planning for future feature roadmaps.

10. Contact & Business Development

Primary Contact

Kulah Jirma

Email: kulah@hydrolifetech.com

Phone: +254 731 206 395

General Inquiries

info@hydrolifetech.com

Website: <https://www.hydrolifetech.com>

11. Case Studies & Portfolio

Hydrolife Tech maintains a robust portfolio of successful projects across government and private sectors, demonstrating our ability to deliver measurable value and complex technical solutions on time and within budget. Our ability to secure and maintain accreditation with Kenya's ICT Authority is a testament to our sustained quality and operational maturity.

12. Executive Summary

Hydrolife Tech Limited is a full-service software engineering firm dedicated to delivering cloud-enabled, user-focused digital solutions across East Africa and internationally. Accredited by Kenya's ICT Authority, Hydrolife Tech combines deep technical expertise, professional agile delivery, and a product-driven mindset to help organizations modernize services, digitize essential workflows, and successfully launch scalable, next-generation software products.

Director: Kulah Jirma — kulah@hydrolifetch.com — +254 731 206 395

Core Services: Custom software development, cloud infrastructure & DevOps, enterprise integrations, mobile application development, UX design, and professional maintenance & support.

Approach: Agile, secure, test-driven, client-focused, and an accredited government supplier.

2. FIRM'S REFERENCES

Relevant Services Carried Out in the Last Five Years That Best Illustrate Qualifications

Using the format below, provide information on each assignment for which your firm either individually, as a corporate entity or in association, was legally contracted.

Reference 1

Assignment Name:	Country:
Provision of Archaeological and Cultural Mapping System	Kenya
Location within Country:	Professional Staff provided by Your Firm/Entity(profiles):
Nairobi/Remote	Team Leader, GIS Specialist, Software Developer, Database Administrator
Name of Client:	Clients contact person for the assignment:
Kivulini Trust	Hadija Hassan
Address:	No of Staff-Months; Duration of assignment:
P. O Box 381 - 000242, Kitengela	12 Staff-Months; approx. 2.5 Months
Start Date (Month/Year):	Completion Date (Month/Year):
February 2025	April 2025
Name of Associated Consultants. If any:	No of Months of Professional Staff provided by Associated Consultants:
N/A	N/A
Name of Senior Staff (Project Director/Coordinator, Team Leader) Involved and Functions:	

Kulah Jirma (Project Director), Mathews Onyango (Project Manager), Chege Danche (Lead Analyst)	
Narrative Description of project:	
Development of a comprehensive digital mapping system to document, archive, and visualize archaeological sites and cultural heritage data. The system allows for secure data entry, geospatial tagging, and retrieval of cultural assets for preservation and research purposes.	
Description of Actual Services Provided by Your Staff:	
• Requirement gathering and system analysis. • Design and development of the web-based mapping portal. • Implementation of GIS features for location plotting. • Database design for high-volume cultural data storage. • User training and system commissioning.	
Approximate Value of Services (Kshs):	8,120,000.06

Reference 2

Assignment Name:	Country:
Design Development and Deployment of Custom Warehouse Management Software	Kenya
Location within Country:	Professional Staff provided by Your Firm/Entity(profiles):

Nairobi	Project Manager, Senior Developer, QA Engineer, Implementation Specialist
Name of Client:	Clients contact person for the assignment:
Andalusi Contractors and Suppliers	Tess Chege
Address:	No of Staff-Months; Duration of assignment:
P.O BOX 34 – 60300 Isiolo	15 Staff-Months; approx. 3 Months
Start Date (Month/Year):	Completion Date (Month/Year):
May 2023	August 2023
Name of Associated Consultants. If any:	No of Months of Professional Staff provided by Associated Consultants:
N/A	N/A
Name of Senior Staff (Project Director/Coordinator, Team Leader) Involved and Functions:	
Kulah Jirma (Project Director), Calvin Njuguna (Lead Developer), Joel Mutisya (Implementation)	
Narrative Description of project:	
Development of a bespoke Warehouse Management System (WMS) tailored to the construction and supply sector. The system handles inventory tracking, stock level alerts, procurement workflows, and dispatch management to optimize supply chain efficiency.	
Description of Actual Services Provided by Your Staff:	
• System architecture design and workflow	

modeling. • Full-stack software development (Backend & Frontend). • Integration with existing procurement processes. • Rigorous testing and deployment to client servers. • Staff training on inventory management modules.	
Approximate Value of Services (Kshs):	14,906,000.00

Reference 3

Assignment Name:	Country:
Supply Installation Testing and Commissioning of Warehouse Management System	Kenya
Location within Country:	Professional Staff provided by Your Firm/Entity(profiles):
Nairobi	Systems Engineer, Backend Developer, Support Specialist
Name of Client:	Clients contact person for the assignment:
Al Shamim Overseas Ltd	Odhiambo Fredrick
Address:	No of Staff-Months; Duration of assignment:
P.O Box 8935 - 00200 Nairobi	10 Staff-Months; approx. 4 Months
Start Date (Month/Year):	Completion Date (Month/Year):

August 2022	November 2022
Name of Associated Consultants. If any:	No of Months of Professional Staff provided by Associated Consultants:
N/A	N/A
Name of Senior Staff (Project Director/Coordinator, Team Leader) Involved and Functions:	
Mathews Onyango (Project Manager), Chege Danche (Technical Lead)	
Narrative Description of project:	
Supply and implementation of an automated warehouse solution to manage import/export stock. The project involved installing the software environment, configuring the database, testing system integrity, and commissioning the final product for live operations.	
Description of Actual Services Provided by Your Staff:	
• Installation and configuration of WMS software. • System testing (Unit testing and User Acceptance Testing). • Data migration of existing stock records. • Commissioning and handover. • Provision of technical manuals	

3. Comments and Suggestions on the Terms of Reference and on Data, Services and Facilities to be Provided by the Procuring Entity

Our project team has conducted a comprehensive review of the Terms of Reference (ToR) for the Development of the Revenue Automation System for the County Government of Isiolo. We find the ToR to be well-structured, clearly identifying the need to automate and enhance revenue collection across key streams, which is consistent with the provisions laid out in the **Isiolo County Finance Act, 2023** (or latest version).

The following comments and suggestions are offered constructively, aimed at defining clear boundaries, mitigating project risks, and ensuring the smooth and successful deployment of a robust, future-proof system.

3.1. Comments and Clarifications on the Terms of Reference (ToR)

While the overall scope is clear, we propose the following clarifications to prevent ambiguity during execution:

Area of Comment	Consultant's Comment/Clarification Request	Rationale for Suggestion
A. Data Migration Scope	The ToR should explicitly define the volume, format, and cleanliness standards for historical data to be migrated (e.g., 3 years of transaction data, current registers).	To accurately scope the effort, timeline, and resource allocation for data cleaning and initial migration, a critical path item.
B. Payment Gateway Integration	The ToR requires the automation system to integrate with existing payment platforms (e.g., M-Pesa, Banks). We recommend that the County formally designates and provides technical specifications/APIs for all required payment	To avoid delays, as third-party payment integrations are often dependent on timely technical support and documentation from external service providers.

	gateways prior to the Project Kick-off.	
C. Compliance with the Finance Act	We recommend the ToR explicitly mandate a sign-off stage where the system's fee/charge configuration is validated by the County's Finance and Legal Departments against the latest Isiolo County Finance Act schedules.	To ensure the system is legally compliant from day one and that all rates (First, Second, and Third Schedules) are correctly implemented.

3.2. Suggestions on Required Data and Information

The success of the implementation hinges on the quality and timely provision of specific, structured source data. We kindly request that the County provides the following essential data sets:

Data Set Required	Source / Description	Format Preference
1. Statutory Rate Schedules	Complete soft copies of the First, Second, and Third Schedules of the Isiolo County Finance Act, 2023 (or latest). This must include all current fees, charges, permits, market cess, and land rates.	Digital, editable format (Excel, CSV, or structured text).
2. Customer & Register Data	The current, clean register data for key revenue streams, including: Business Permit Holders Register, Land Rates Register, Plot/House Rent Ledger, and Parking Permits Register.	Digital, structured format (Excel, CSV) with unique identifiers and geo-location details (where applicable).
3. Organizational	The current organogram of	Document or Spreadsheet.

Structure & Users	the revenue collection departments, detailing roles and hierarchy, to define user permissions and workflows (e.g., approval limits, cash office staff, enforcement roles).	
4. Geo-Spatial Assets	GIS maps or detailed boundary information for revenue collection zones, including municipal boundaries, sub-county offices, markets, and designated parking areas.	Shapefiles (GIS format) or high-resolution maps.

3.3. Suggestions on Required Services and Facilities

To ensure the Consulting team operates efficiently and that the project remains on schedule, we propose that the Procuring Entity commit to providing the following services and facilities, as anticipated in **Appendix D** of the RFP:

A. Dedicated Project Resources and Personnel

1. **County Project Manager (Mandatory):** Designation of a single, high-level, and empowered County representative to act as the primary Project Manager. This individual must have the authority to grant approvals and make timely decisions regarding scope and configuration.
2. **Subject Matter Experts (SMEs):** The continuous availability of key staff from the Finance, Trade, Lands, and ICT departments for workshops, data validation, system configuration, and User Acceptance Testing (UAT).
3. **Authentication/Access:** Timely provision of necessary access credentials, network privileges, and security clearances for Consultant personnel to access County data and systems required for integration and testing.

B. Technical and Infrastructure Facilities

1. **Hosting Environment:** Clear definition of whether the system will be hosted on County infrastructure (on-premise) or a Cloud platform. If on-premise, provision of a secure, dedicated Server Environment (Virtual Machine or Physical Server) with the minimum specifications to be provided by our team.
2. **UAT and Training Facility:** Access to a stable internet connection and a dedicated UAT lab (computer room) for system configuration, intensive testing, and end-user training

sessions for the duration of the engagement.

C. Physical Facilities

1. **Secure Office Space:** Provision of a dedicated, secure, furnished, and air-conditioned office space within a convenient County facility for the Consultant's core team (minimum four workstations) for the duration of the project, complete with stable internet and power access.

4. Description of the Methodology and Work Plan for Performing the Assignment

Hydrolife Tech Limited proposes an **Agile/Scrum Methodology** tailored to our **8-Week Accelerated Delivery Framework** to develop and implement the Isiolo Revenue Automation System (RAS). This approach is specifically chosen to manage the aggressive timeline while maintaining high standards for security, quality, and stakeholder involvement.

4.1 Implementation Methodology: Accelerated Agile Scrum

Our methodology prioritizes working software over exhaustive documentation and continuous collaboration over rigid processes. This accelerated approach ensures that the County Government sees functional progress every two weeks.

(i) Principles of the Methodology

- Iterative Delivery:** The project is broken down into four (4) two-week Sprints, with functional components delivered incrementally.
- High-Level Collaboration:** Daily stand-up meetings (Scrums) will ensure the Project Manager (Mathews) has real-time visibility into progress and roadblocks.
- Risk Mitigation:** By integrating Quality Assurance (QA) and User Acceptance Testing (UAT) from Week 5 onwards (Phases III and IV), we detect and fix issues early, preventing costly delays later.
- Security-First Development:** The Lead System Architect (Danche) integrates security standards (Security by Design) from the architecture stage (Week 1) through development (Weeks 3-6) and final auditing (Week 7).

(ii) Project Phasing and Execution Model

The 8-week timeline is divided into four sequential phases, which align directly with the project milestones and reporting requirements:

Phase	Duration	Core Focus	Key Deliverable
I: Inception & Analysis	Weeks 1–2	Detailed Requirements Elicitation, Secure Architecture Design, Technical Setup.	Inception Report
II: Development & Integration	Weeks 3–6	Core Backend API Development (Golang), Frontend	Interim Report

		UI/UX (React/Flutter), Payment Gateway Integration.	
III: QA & UAT	Weeks 5–7	Comprehensive Functional Testing, Security Audits, User Acceptance Testing with Isiolo Staff, Bug Fixing.	Draft Final Report
IV: Deployment & Handover	Weeks 7–8	Production Environment Deployment (Go-Live), System Administration Training, Documentation Finalisation, Source Code Handover.	Final Report

4.2 Work Plan for Technical Execution

The work plan is divided into two parallel development tracks, allowing simultaneous progress and efficient use of the specialised team members.

Track A: Backend, Architecture, and Infrastructure (Lead: Chege Danche)

This track focuses on the foundational, non-visible elements of the system, ensuring stability, security, and scalability.

Activity	Description	Primary Weeks
System Architecture Setup	Finalise microservices architecture (Docker, AWS) and set up the production and staging environments.	Wk 1–2
Core API Development (Golang)	Develop high-performance REST APIs for authentication, data	Wk 3–5

	retrieval, business logic, and reporting features.	
Payment Gateway Integration	Integrate, test, and secure all external payment channels (e.g., M-PESA, major banks) into the Golang APIs.	Wk 4–6
Security Hardening	Implement server hardening, access controls, and perform initial vulnerability scans.	Wk 6–7

Track B: Frontend, Database, and User Experience (Lead: Calvin Njuguna)

This track focuses on the user-facing applications and efficient data management.

Activity	Description	Primary Weeks
Database Schema Design	Design the optimal database structure (e.g., PostgreSQL) to support high-volume transactions and reporting queries.	Wk 2–3
Web Admin Portal Development (React)	Develop the administrative interface for billing, user management, and detailed revenue reporting.	Wk 3–5
Mobile App Development (Flutter)	Develop the Field Collector App for on-site payment collection and data verification.	Wk 3–5
API Integration and Data Binding	Connect all frontend components seamlessly with the backend APIs developed in Track A.	Wk 5–6

4.3 Integrated Quality and Acceptance Plan

Quality Assurance and User Acceptance are not treated as separate final steps but are integrated throughout the development process.

Activity	Weeks	Responsible	Purpose
Continuous Integration Testing	Wk 3–6	Lead System Architect/Software Engineer	Automated testing of new features to ensure no regressions and immediate bug detection.
Comprehensive QA Testing	Wk 5–6	Cybersecurity & QA Specialist (Joel)	Execution of detailed test cases covering functional, usability, performance, and cross-browser/device compatibility.
User Acceptance Testing (UAT)	Wk 6–7	Cybersecurity & QA Specialist (Joel)	County staff test the system with real-world scenarios, ensuring the solution meets their specific operational needs.
Security Auditing	Wk 7	Cybersecurity & QA Specialist (Joel)	Final independent review of the deployed production environment to ensure adherence to best practice and data privacy laws.

This integrated work plan, guided by the Accelerated Agile methodology, provides the County Government of Isiolo with the confidence that the Revenue Automation System will be

delivered on time, within budget, and to the highest standards of quality and security.


5. Team Composition and Task Assignments

Hydrolife Tech Limited has assembled a highly skilled and cohesive project team tailored specifically for the rapid 8-Week Accelerated Delivery Framework. Our team members possess the exact technical, managerial, and analytical skills necessary to ensure the successful design, development, and deployment of the Isiolo Revenue Automation System (RAS).

The structure is designed for efficiency and rapid collaboration, with clear segregation of duties across four core service areas, ensuring every aspect of the project—governance, architecture, development, and quality—is expertly managed.

5.1 Project Team Structure and Key Roles

The project team comprises four (4) key personnel, each assigned a critical function, with the overall structure managed by the IT Project Manager to ensure seamless stakeholder communication and project governance.

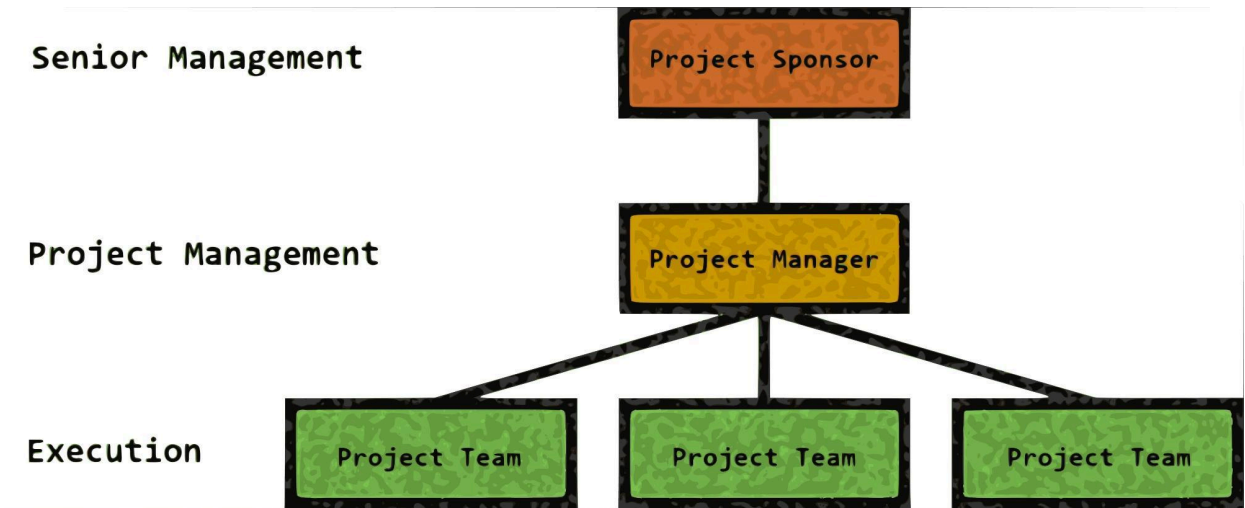

Role (Service Area)	Key Personnel	Primary Function
IT Project Manager (Systems Analysis & Design)	Mathews Onyango Ong'any	Project governance, requirements analysis, risk management, and client liaison.
Lead System Architect	Chege Danche Ng'ang'a	Technical authority, Golang

(Software Development Services)		backend development, secure architecture design, and DevOps/Cloud Infrastructure management.
Lead Software Engineer (Database & Infrastructure Services)	Calvin Njuguna Ngugi	Frontend (Web/Mobile) development, User Experience (UX), database schema design, and API integration.
Cybersecurity & QA Specialist (Cybersecurity & Quality Assurance Services)	Joel Ngite Mutisya	Comprehensive Quality Assurance (QA) testing, security compliance, and direct UAT support.

5.2 Detailed Task Assignments per Role

Each team member has a detailed set of tasks aligned with their core competencies, ensuring complete coverage of the Statement of Work.

(i) Mathews Onyango Ong'any (IT Project Manager)

Mr. Onyango is the head of the project and the primary point of contact. His role ensures the project remains on schedule and within scope.

- **Project Governance:** Manage the overall project lifecycle, ensuring strict adherence to the **8-Week Accelerated Delivery Framework**.
- **Systems Analysis:** Lead detailed requirements gathering, system specification, and process documentation for all modules (Billing, Payments, Reporting).
- **Stakeholder Management:** Act as the primary liaison between the technical team and County management.
- **Risk Management:** Implement proactive risk mitigation strategies, manage project scope changes, and ensure timely delivery of all project milestones (Inception, Interim, Draft Final, Final Reports).

(ii) Chege Danche Ng'ang'a (Lead System Architect / DevOps)

Mr. Danche is the technical authority, responsible for the core infrastructure and secure architecture.

- **System Architecture Design:** Design the secure, containerized architecture using **Docker and AWS** to ensure the system is functional, secure against cyber threats, and scalable.

- **Lead Track A (Backend/DevOps):** Focus on the development of high-performance **Golang APIs** and manage the entire AWS Infrastructure setup.
- **Database Schema:** Collaborate on the design and optimization of the core database schema to support microservices.
- **Implementation Oversight:** Oversee the backend logic and DevOps streams, ensuring code quality and deployment efficiency.

(iii) Calvin Njuguna Ngugi (Lead Software Engineer / Database & Infrastructure)

Mr. Ngugi is responsible for the user-facing applications and core data management.

- **Lead Track B (Frontend/Database):** Responsible for the client-facing user experience, covering both the **Web Admin Portal (React)** and the **Field Collector Mobile App (Flutter)**.
- **Database Design & Integration:** Design and implement the optimal database schema (SQL Server/PostgreSQL/Firebase) to support high-volume revenue data and backend logic.
- **API Integration:** Ensure rapid and seamless integration between the frontend applications and the Golang microservices backend.
- **Deployment Support:** Assist the Lead System Architect in cloud infrastructure setup and configuration to ensure system availability and performance.

(iv) Joel Ngige Mutisya (Cybersecurity & QA Specialist)

Mr. Mutisya's primary focus is on system robustness, correctness, and security compliance.

- **Quality Assurance (QA) Testing:** Develop and execute comprehensive test plans across all system modules (Billing, Payments, Reporting) to ensure functionality and robustness.
- **Security & Compliance:** Assist in the implementation of cybersecurity best practices, process documentation, and initial vulnerability checks.
- **UAT Support:** Provide direct support during User Acceptance Testing (UAT) with County staff, documenting and resolving reported issues in real-time.
- **System Documentation:** Contribute to the creation of the technical and user manuals.

This team composition ensures that all aspects of the Revenue Automation System—from high-level planning and secure architecture to detailed code implementation and final quality assurance—are managed by seasoned professionals with relevant and verifiable experience.

Proposed Position: Database & Infrastructure Services (Lead Software Engineer)

Name of Firm: Hydrolife Tech Limited

Name of Staff: Calvin Njuguna Ngugi

Profession: Full Stack Software Engineer

Date of Birth: 1999-05-21

Years with Firm: 4

Nationality: Kenyan

Membership in Professional Societies:

Detailed Tasks Assigned:

- **Lead Track B (Frontend/Database):** Responsible for the client-facing user experience, covering both the Web Admin Portal (React) and the Field Collector Mobile App (Flutter).
- **Database Design & Integration:** Design and implement the optimal database schema (SQL Server/PostgreSQL/Firebase) to support high-volume revenue data and backend logic.
- **API Integration:** Ensure rapid and seamless integration between the frontend applications and the Golang microservices backend.
- **Deployment Support:** Assist in cloud infrastructure setup and configuration to ensure system availability and performance.

Key Qualifications:

Mr. Calvin Njuguna is a Professional Full Stack Software Engineer with deep expertise in both frontend (React, NextJs) and backend (Java Maven, Laravel, Node.js) development. He is designated as the Database & Infrastructure Services expert due to his proficiency in managing diverse database technologies, including **Microsoft SQL Server** for relational data and **Firebase** for non-relational data, which is crucial for handling the varied data needs of a Revenue Automation System.

His specialization in **Flutter/Dart** is essential for developing the robust, offline-capable mobile application for field revenue collection, ensuring a smooth and user-friendly experience (UX). His experience in **Agile development** and leading development projects for comprehensive management systems ensures he can deliver high-quality, fully integrated solutions within the accelerated project timeline. His role is central to translating the systems analysis into a functional, user-facing, and data-backed reality.

Relevant Experience Highlights:

- **Full Stack Development:** Led development for a comprehensive hotel management system, including backend (Java Maven) and frontend (NextJs).
- **Database Management:** Proficient in using both relational (MS SQL Server) and non-relational (Firebase) database technologies.
- **Deployment & User Support:** Experience in application deployment, user orientation, and ensuring seamless operational support.

–

Education:

- Software Engineering
Moringa School
Dates: June 2022 – January 2023
- Bachelor of Science: Information Technology
Kabarak University
Dates: 2017 – 2021
- Google IT support and Networking
[Provider]
Dates: August 2020 – November 2020

–

Employment Record:

From: October 2021 To: Present

Employer: Hydrolife Tech Limited

Position: Full Stack Developer

Location: Nairobi, Kenya

Summary: Led backend development for a comprehensive hotel management system (Java Maven). Built frontend features using NextJs, ensuring a high-quality user experience.

From: July 2021 To: September 2023

Employer: Techware Enterprises Limited

Position: Full Stack Developer

Location: Nairobi, Kenya

Summary: Developed and maintained systems using Laravel, React, and Bootstrap. Managed application deployment and provided user training and support, ensuring seamless operation.

From: February 2020 To: April 2020

Employer: NCBA Bank

Position: Attachment - Credit Analyst

Location: Nairobi, Kenya

Summary: Conducted data entry to the database from files. Reviewed consumer credit data to assess their financial situation.

–

Certification:

I, the undersigned, certify that these data correctly describe me, my qualifications, and my experience.

Date: _____

[Signature of staff member]

Date: _____

[Signature of authorized representative of the firm]

Full name of staff member: Calvin Njuguna Ngugi

National ID: 36519838

Full name of authorized representative: _____

Proposed Position: Software Development Services

Name of Firm: Hydrolife Tech Limited

Name of Staff: Chege Danche Ng'ang'a

Profession: Software Engineer

Date of Birth: 1999-04-26

Years with Firm: 5 Years

Nationality: Kenyan

Membership in Professional Societies: ISACA (CSX Cybersecurity Fundamentals)

Detailed Tasks Assigned:

- **Lead System Architect (Backend/DevOps):** Serve as the technical authority for the project, managing Cloud Infrastructure and Security.
- **Lead Track A (Backend/DevOps):** Focus on the development of Golang APIs, Database Schema design, and AWS Infrastructure setup.
- **System Architecture Design:** Design the secure, containerized architecture using Docker and AWS to ensure the system is functional, secure against cyber threats, and scalable.
- **Implementation:** Oversee the backend logic and DevOps streams within the 8-week accelerated delivery framework.

Key Qualifications:

Mr. Chege Danche is a seasoned Software Engineer with extensive experience in the design, development, and implementation of **Revenue Automation Systems, ERP solutions, and Fintech applications**. He possesses a unique blend of skills in full-stack development (Golang, Flutter, Dart), microservices architecture, and payment gateway integrations.

Most notably, he served as a **Lead Developer for the Kiambu County ERP**, where he successfully developed and implemented a **Revenue Collection System**. His responsibilities included integrating secure payment gateways, developing real-time revenue monitoring dashboards, and automating reporting tools. This direct experience with County Government revenue automation makes him uniquely qualified for the Isiolo County assignment.

Additionally, his tenure at **SasaPay** demonstrates deep expertise in **financial technologies**, including USSD development, Anti-Money Laundering (AML) system integration, and the creation of developer SDKs for payment APIs. He is proficient in cloud computing (AWS, GCP, Azure), database management (PostgreSQL, MongoDB),

and system security.

Relevant Experience Highlights:

- **Kiambu County Revenue Collection System:** Developed robust ERP modules for revenue collection, payment gateway integration, and data analytics.
- **SasaPay (Fintech):** Engineered backend microservices for payments, USSD applications, and financial security systems.
- **IPOS Systems:** Developed scalable APIs for sales and inventory management, crucial for POS-based revenue collection.

—

Education:

- Msc Laser Technology (Ongoing)
Multimedia University of Kenya
Dates: [Current]
- Bsc Applied Physics and Computer Science
Multimedia University of Kenya
Dates: Aug 2017 – Dec 2021
Degree: Bachelor of Science (Second Class Honors, Upper Division)
- Kenya Certificate of Secondary Education
Kangema High School
Dates: Jan 2013 – Dec 2016
Grade: A- (74 points)
- **Specialized Training & Certifications:**
 - **Cloud Dev-ops**, ALX/Udacity (July 2022 – Sept 2022)
 - **CSX Cybersecurity Fundamentals**, ISACA (Nov 2019)
 - **Cloud Computing**, Amazon Web Services (Sept 2019 – Dec 2019)
 - **HCIA - Routing and Switching**, Multimedia University Huawei Academy (Feb 2019 – May 2019)

—

Employment Record:

From: February 2021 To: Present

Employer: Hydrolife Tech Limited

Position: Backend & Desktop App Developer

Location: Nairobi, Kenya

Summary: Developing Golang scalable APIs for sales and inventory; maintaining

offline-capable desktop POS applications using Flutter and Dart.

From: November 2024 To: Present

Employer: freelance with Ibibe Games

Position: Game Engine Backend Developer

Location: Nairobi.

Summary: Developing backend solutions for high-transaction environments; designing game management systems and APIs.

From: June 2024 To: Present

Employer: Consultancy for Kiambu County Government

Position: Software Developer and Lead Developer (County ERP)

Location: Kiambu, Kenya

Summary: Lead role in developing the County ERP for Revenue Collection.

Implemented secure payment gateways, automated reporting tools, and integrated GIS for Lands Management and Physical Planning systems.

From: September 2022 To: June 2024

Employer: SasaPay, Viewtech

Position: Backend and Microservices Engineer

Location: Nairobi, Kenya

Summary: Developed USSD applications, backend microservices for financial transactions, and AML systems. Managed Developer SDKs and integrated REST/GraphQL APIs.

From: September 2022 To: Dec 2022

Employer: Onekitty, Liana Technologies Limited

Position: Software Engineer

Location: Nairobi Kenya

Summary: Spearheaded backend infrastructure using Golang and microservices.

Integrated payment gateways (Mpesa, Airtel Money, SasaPay, Banks).

From: August 2022 To: January 2023

Employer: Skills App

Position: Technical Lead and Golang Developer

Location: Nairobi

Summary: Led a team of developers; defined technical strategy and built backend infrastructure using Golang and MongoDB.

From: August 2022 To: September 2022

Employer: Tanda Africa (Fintech)

Position: Microservices Developer (Consultant)

Location: Nairobi

Summary: Developed microservices using Golang, Kafka, and MongoDB; led payment integration teams.

From: April 2021 To: July 2022

Employer: Veeta, UK

Position: Software Developer

Location: Remote / UK

Summary: Designed responsive UI using Flutter and integrated backend REST APIs using Golang.

From: February 2021 To: June 2022

Employer: Topit, Dallas USA

Position: Senior Software Engineer

Location: Remote / USA

Summary: Utilized Golang for backend development, multi-threading, and GraphQL API integration.

From: July 2020 To: February 2022

Employer: E & M Tech

Position: Software Engineer (Fintech/Finacle Integrations)

Location: Nairobi

Summary: Advanced Human Resource Management Systems; engineered backend using Spring Boot Java and Golang.

From: January 2020 To: March 2020

Employer: National Youth Service

Position: Information Technology Support Engineer

Location: Kenya

Summary: Maintained ICT infrastructure and conducted cybersecurity awareness training.

From: September 2019 To: November 2019

Employer: Kenya Education Network (KENET)

Position: Data Collection Officer

Location: Nairobi, Kenya

Summary: Surveyed internet connectivity and analyzed student feedback.

–

Certification:

I, the undersigned, certify that these data correctly describe me, my qualifications, and my experience.

Date: _____

[Signature of staff member]

Date: _____

[Signature of authorized representative of the firm]

Full name of staff member: Chege Danche Ng'ang'a

Full name of authorized representative: _____

Proposed Position: Cybersecurity & Quality Assurance Services

Name of Firm: Hydrolife Tech Limited

Name of Staff: Joel Ngite Mutisya

Profession: Junior Developer / IT Support Specialist

Date of Birth: 2000-11-15

Years with Firm: 4

Nationality: Kenyan

Membership in Professional Societies:

Detailed Tasks Assigned:

- **Quality Assurance (QA) Testing:** Develop and execute comprehensive test plans across all system modules (Billing, Payments, Reporting) to ensure functionality and robustness.
- **Security & Compliance:** Assist in the implementation of cybersecurity best practices, process documentation, and initial vulnerability checks (relevant to his Cloud Computing certification).
- **UAT Support:** Provide direct support during User Acceptance Testing (UAT) with County staff, documenting and resolving reported issues.
- **System Documentation:** Contribute to the creation of the technical and user manuals.

Key Qualifications:

Mr. Joel Mutisya is an energetic and detail-oriented professional assigned to the crucial role of Cybersecurity and Quality Assurance (QA). With a background as a Junior Developer and IT Support Officer, he possesses direct experience in systems administration, troubleshooting, and delivering user-focused solutions, making him ideal for rigorous QA testing.

His technical skills include PHP (Laravel), JavaScript, and MySQL, allowing him to understand the underlying logic of the Revenue Automation System and perform in-depth white-box testing and debugging. Critically, he holds an **HCIA – Cloud Computing** certification, providing foundational knowledge necessary to verify the security and proper deployment of the system's cloud environment, ensuring it meets required security benchmarks against cyber threats. His proven ability to document processes and provide user training will be vital during the UAT and system handover phases.

Relevant Experience Highlights:

- **QA & Bug Fixing:** Hands-on experience collaborating in Agile teams to deliver new features, bug fixes, and system improvements.
- **IT Support & Systems Administration:** Oversaw system installations, network administration, and end-user support at KICOTEC.
- **Cloud Knowledge:** HCIA – Cloud Computing certification is directly applicable to ensuring the security and integrity of the AWS-based infrastructure.

–

Education:

- BSc. Information Technology
South Eastern Kenya University
Dates: 2020–2024
Degree: Second Class Upper Division
- HCIA – Cloud Computing
Huawei Talent Online
Dates: 2022

–

Employment Record:

From: September 2021 To: Present

Employer: Hydrolife Tech Limited

Position: Senior Developer

Location: Nairobi, Kenya

Summary: Developing and maintaining client applications with secure back-end logic and responsive user interfaces. Collaborating in Agile teams to deliver new features, bug fixes, and system improvements using PHP & JavaScript.

From: March 2025 To: August 2025

Employer: AO Software Development Company

Position: Senior Developer

Location: Nairobi, Kenya

Summary: Assisted in application feature development, debugging, and UI enhancements. Supported Agile sprints by documenting tasks and implementing fixes.

From: April 2024 To: October 2024

Employer: KICOTEC (Kitui County Textile Company)

Position: IT Support Officer

Location: Kitui, Kenya

Summary: Oversaw system installations, network administration, and end-user support. Provided training and troubleshooting for staff across the company.

From: October 2023 To: February 2024

Employer: Get-Cash Capital Lending Solution

Position: Intern

Location: Nairobi, Kenya

Summary: Conducted database reconciliations and system diagnostics. Delivered user training and technical support to enhance service delivery.

From: May 2023 To: August 2023

Employer: Mwingi General Hospital

Position: Industrial Attachment

Location: Mwingi, Kitui County, Kenya

Summary: Supported Hospital Management System (HMS) maintenance and upgrades. Ensured patient data security and assisted in troubleshooting hospital ICT systems.

–

Certification:

I, the undersigned, certify that these data correctly describe me, my qualifications, and my experience.

Date: _____

[Signature of staff member]

Date: _____

[Signature of authorized representative of the firm]

Full name of staff member: Joel Ngite Mutisya

National ID: 38671578

Full name of authorized representative: _____

Proposed Position: Systems Analysis & Design (IT Project Manager)

Name of Firm: Hydrolife Tech Limited

Name of Staff: Mathews Onyango Ong'any

Profession: IT Project Manager / Systems Analyst

Date of Birth: 1994-08-03

Years with Firm: 6

Nationality: Kenyan

Membership in Professional Societies: PMP Certification, ITIL Foundation

Detailed Tasks Assigned:

- **Project Governance:** Manage the overall project lifecycle, ensuring adherence to the 8-Week Accelerated Delivery Framework.
- **Systems Analysis:** Lead requirements gathering, detailed system specification, and process documentation for the Revenue Automation System (RAS).
- **Stakeholder Management:** Act as the primary liaison between the technical team and County management, ensuring project alignment and managing communication.
- **Risk Management:** Implement risk mitigation strategies, manage project scope, and ensure timely delivery of all project milestones (Inception, Interim, Draft Final, Final Reports).

Key Qualifications:

Mr. Mathews Onyango is a highly experienced IT Project Manager with over 6 years of expertise in leading and delivering complex, large-scale technology initiatives within the highly regulated Banking and Telecommunications sectors (including Safaricom). His profound knowledge of project methodologies, including **Agile/Scrum** and **ITIL**, is crucial for ensuring the rapid and efficient implementation of the Isiolo Revenue Automation System (RAS).

His experience includes managing critical projects involving **Core Banking Systems**, **Mobile Money Platforms (M-PESA)**, and **Siebel CRM** integrations. This background demonstrates mastery in managing projects that involve high transaction volumes, sensitive financial data, and complex system integrations—all directly relevant to a County Revenue System. He is skilled in technical oversight, resource planning, risk management, and bridging the gap between technical teams and business stakeholders, a vital function for the successful rollout of RAS. He has technical

exposure to databases such as **Oracle, SQL Server, and PostgreSQL.**

Relevant Experience Highlights:

- **Safaricom PLC:** Led high-impact integration projects generating over KES 2B+ in combined revenues and coordinating teams for projects like M-PESA Go.
- **AO Technology Group:** Managed core banking system enhancements, supporting over 700K users and ensuring compliance with ITIL processes.
- **Systems Delivery:** Proven track record in full project lifecycle delivery, from requirements gathering to post-implementation handover.

—

Education:

- BSc. Information Communication Technology and Management
Maseno University
Dates: 2016 – 2021
- **CERTIFICATIONS (In Progress/Planned):**
 - **ITIL Foundation**
 - **Project Management Professional (PMP)**
 - **Microsoft SQL Server (MCP)**

—

Employment Record:

From: Mar 2019 To: Present

Employer: Hydrolife Tech Limited.

Position: IT Project Engineer (Full Stack/Integration Projects)

Location: Nairobi, Kenya

Summary: Led multiple IT projects integrating Siebel CRM with ERP systems, ensuring smooth data flow for 40M+ customers. Coordinated cross-functional teams to deliver high-impact financial products. Applied project management methodologies to ensure timely delivery and risk management.

From: January 2023 To: October 2024

Employer: AO Technology Group

Position: IT Project Coordinator / Backend Developer

Location: Nairobi, Kenya

Summary: Managed enhancements to the core banking system supporting 700K+

users. Directed project lifecycle from requirements gathering to deployment, ensuring scalability and compliance with ITIL. Mentored junior developers.

From: January 2022 To: August 2022

Employer: Podii Consultancy

Position: Software Engineer Trainee (Project Support)

Location: Nairobi, Kenya

Summary: Contributed to IT projects enhancing M-PESA APIs and ERP systems.

Supported database upgrades, system testing, and reporting tasks within project frameworks.

From: May 2019 To: August 2019

Employer: Technical University of Kenya (TUK)

Position: IT Intern

Location: Nairobi, Kenya

Summary: Supported IT infrastructure upgrade projects including server systems, user profile migrations, and database reporting.

–

Certification:

I, the undersigned, certify that these data correctly describe me, my qualifications, and my experience.

Date: _____

[Signature of staff member]

Date: _____

[Signature of authorized representative of the firm]

Full name of staff member: Mathews Onyango Ong'any

National ID: 34215099

Full name of authorized representative: _____

Njuguna Ngu gi	are Engineer (Frontend/Database)								
Joel Ngite Mutisya	Cybersecurity & QA Specialist	Half	Half	Half	Half	Full	Full	Full	Half
Total Staff-Weeks Committed:	8 Weeks	2.5	3.5	3.5	3.5	4.0	4.0	3.0	2.5

7.2 Schedule Rationale

The distribution of effort ensures maximum efficiency and reflects a standard Agile implementation approach:

1. Inception & Analysis (Weeks 1-2):

- **Mathews Onyango (IT Project Manager)** dedicates **Full** time to detailed requirements gathering, process mapping, and finalising the System Specification Document.
- **Chege Danche (Lead System Architect)** dedicates **Full** time to finalising the secure system architecture and setting up the core AWS/Docker environment.
- The Lead Software Engineer and QA Specialist are engaged at **Half** time to provide technical input on feasibility and non-functional requirements.

2. Development & Integration (Weeks 3-6):

- **Chege Danche** (Backend/DevOps) and **Calvin Njuguna** (Frontend/Database) are at **Full** time during this core development sprint, building the Golang APIs, Web Portal, and Mobile App.
- **Joel Ngite** (QA) shifts to **Full** time in Weeks 5 and 6 to begin iterative functional and load testing as modules are completed.

3. Testing, UAT, & Final Reports (Week 7):

- **Joel Ngite** (QA) is at **Full** capacity, leading User Acceptance Testing (UAT) with County staff and conducting final security audits.
- The Lead Architect and Lead Software Engineer scale back to **Half** time for issue resolution and final system tuning.

4. **Deployment & Handover (Week 8):**

- **Mathews Onyango** (Project Manager) returns to **Full** time to manage the final deployment, sign-offs, source code handover, and the creation of the Final Report.
- The technical team is at **Half** capacity, providing final deployment support, system administration training, and documentation completion.

This schedule guarantees dedicated and staggered resource allocation, concentrating expertise where it is most needed at each critical stage of the 8-week project.

8. Activity (Work Schedule)

The comprehensive work schedule outlines the specific activities, milestones, and deliverables planned across the 8-Week Accelerated Delivery Framework. This schedule ensures transparent tracking, proactive risk management, and the rapid deployment of a fully functional Revenue Automation System (RAS).

The schedule is structured across four (4) distinct, overlapping phases: Inception & Analysis, Development & Integration, Quality Assurance & UAT, and Deployment & Handover.

8.1 Detailed Work Breakdown Structure (WBS)

The following table provides the detailed schedule, where an 'X' denotes the primary weeks in which the activity will be executed.

Activ ity/T ask	Resp onsi ble Role(s)	Wk 1	Wk 2	Wk 3	Wk 4	Wk 5	Wk 6	Wk 7	Wk 8
Phas e I: Ince ption & Anal ysis (Wee ks 1-2)									
1.1 Proje ct Kick- off & Team Mobil isatio n	IT Proje ct Mana ger (Mat hews)	X							
1.2	IT	X	X						

Detailed Requirements Gathering (Functional & Non-Functional)	Project Manager (Mathews)								
1.3 Final System Specification & Process Mapping	IT Project Manager (Mathews)		X						
1.4 Milestone: Inception Report Submission	IT Project Manager (Mathews)		X						
1.5 Finalise System	Lead System Architect	X	X						

Architecture & Tech Stack Setup	(Danche)								
Phase II: Development & Integration (Weeks 2-6)									
2.1 Database Schema Design & Setup	Lead Software Engineer (Calvin)		X	X					
2.2 Golang Microservices Backend Development (APIs)	Lead System Architect (Danche)			X	X	X			

)									
2.3 Web Admin Portal (React) Development (Billing, Reporting)	Lead Software Engineer (Calvin)			X	X	X			
2.4 Field Collector Mobile App (Flutter) Development (Payments)	Lead Software Engineer (Calvin)			X	X	X			
2.5 Payment Gateway Integration	Lead System Architect (Danche)				X	X	X		

(M-P ESA, Bank s)									
2.6 Full System API Integration (Frontend/ Backend)	Lead Software Engineer (Calvin)					X	X		
2.7 Milestones: Interim Report Submission	IT Project Manager (Matthews)					X			
Phase III: Quality Assurance & UAT (Weeks 5-7)									
3.1 Unit	Lead System			X	X	X	X		

Testi ng and Integ ratio n Testi ng (Cont inuou s)	m Archi tect/ Softw are Engin eer								
3.2 Com preh ensiv e QA Testi ng & Issue Loggi ng	Cybe rsecu rity & QA Speci alist (Joel)					X	X		
3.3 Secu rity Audit s & Vulne rabilit y Chec ks	Cybe rsecu rity & QA Speci alist (Joel)						X	X	
3.4 User Acce ptanc e Testi ng (UAT)	Cybe rsecu rity & QA Speci alist (Joel)						X	X	

with Coun ty Staff									
3.5 Bug Fixin g and Syste m Refin emen t	Lead Syste m Archi tect/ Softw are Engin eer						X	X	
3.6 Miles tone: Draft Final Repo rt Sub missi on	IT Proje ct Mana ger (Mat hews)							X	
Phas e IV: Depl oym ent & Hand over (Wee ks 7-8)									
4.1 Prod uctio n Envir	Lead Syste m Archi tect							X	

onment Deployment (RAS Go-Live)	(Dan che)								
4.2 System Administration Training & Knowledge Transfer	IT Project Manager (Matthews)							X	X
4.3 Technical & User Manual Hand over	IT Project Manager (Matthews)								X
4.4 Final Source Code Hand over & Project	IT Project Manager (Matthews)								X

Closure									
4.5 Milestone: Final Report & Acceptance Certificate	IT Project Manager (Matthews)								X

8.2 Project Phasing and Deliverables

The 8-week plan ensures that key deliverables are submitted at structured intervals, allowing the County Government of Isiolo constant visibility and control:

- **Inception (Week 2):** Submission of the **Inception Report**, detailing finalised requirements and System Architecture.
- **Interim (Week 5):** Submission of the **Interim Report**, confirming the completion of core backend APIs and initial UI components, along with a functional demonstration of a payment module.
- **Draft Final (Week 7):** Submission of the **Draft Final Report**, including UAT results, comprehensive test logs, and draft System/User Manuals.
- **Final (Week 8):** Submission of the **Final Report**, Acceptance Certificates, Source Code Handover, and commencement of the Warranty Period.

This detailed work schedule is the foundation of our commitment to the Accelerated Delivery Framework, guaranteeing that every activity is accounted for and delivered on time.

KNOWLEDGE TRANSFER AND CAPACITY BUILDING PLAN

1. Overview and Objectives

Hydrolife Tech Limited recognizes that the success of the Revenue Automation System (RAS) depends not just on technology, but on the people using it. Our Capacity Building Plan is designed to ensure a seamless transition from manual to automated processes, ensuring sustainability and long-term ownership by the County Government of Isiolo.

Key Objectives:

- 1. **Operational Proficiency:** Ensure revenue collectors and cashiers can effectively use POS terminals and the web portal for daily collections and reconciliation.
- 2. **Strategic Oversight:** Equip Executive and Senior Management with skills to interpret BI dashboards for decision-making.
- 3. **Technical Sustainability (KSTA):** Transfer deep support skills to the County ICT team to manage, troubleshoot, and maintain their operations deployment.
- 4. **Change Adoption:** Minimize user resistance through a structured Change Management program.

2. Training Methodology

We utilize a **Role-Based Training Approach**, delivering customized curriculum to three distinct user groups. Training will be conducted using a "Train-the-Trainer" model where applicable, and will include hands-on practical sessions, live simulations, and competency assessments.

Lead Trainer: Joel Mutisya (Implementation & Training Lead)

3. Training Tracks and Curriculum

Track 1: Executive & Senior Management (Strategic Track)

- **Target Audience:** Chief Officers, Directors, Sub-County Administrators.
- **Duration:** 3 Days (Workshop Setting).
- **Focus:** Analytics, Security, and Oversight.

Module	Content	Learning Outcome
Exec-01: System Overview	High-level architecture, security features, and	Understanding the scope and security of the RAS.

	revenue streams overview.	
Exec-02: Business Intelligence	Navigating the Executive Dashboard, interpreting real-time graphs (Daily Collection vs Target), generating executive summaries.	Ability to make data-driven decisions based on real-time revenue trends.
Exec-03: Approval Workflows	Managing waivers, voiding transactions, and audit trail review.	Effective oversight and prevention of revenue leakage.

Track 2: Revenue Authority Staff (Operational Track)

- **Target Audience:** Revenue Collectors, Cashiers, Enforcement Officers, Accountants.
- **Duration:** 5 Days (Hands-on Sessions).
- **Focus:** Daily Operations, POS Usage, Reconciliation.

Module	Content	Learning Outcome
Ops-01: POS Operations	Device handling, log in/out, billing unstructured revenue (Parking, Cess), printing receipts, troubleshooting connectivity.	Proficiency in using Android POS terminals for field collection.
Ops-02: Web Portal Billing	Generating e-slips for structured revenue (Land Rates, SBP), customer registration, and validation.	Accurate billing and invoicing of citizens.
Ops-03: Enforcement	Using the App to verify payment status (QR code scanning), clamping/impounding logs.	Effective enforcement and compliance monitoring.
Ops-04: Reconciliation	Cash handling, M-Pesa/Bank reconciliation, handling suspense payments, daily	Accurate financial reporting and cash management.

	cashing out.	
--	--------------	--

Track 3: ICT Officers (Support & Administration Track)

- **Target Audience:** County ICT Staff (Minimum 5 Officers).
- **Duration:** 5 Days (Technical Support Workshop).
- **Focus:** System Administration, First-Line Support, Troubleshooting.

Module	Content	Learning Outcome
Supp-01: Functional Architecture	Overview of system components, data flow between POS/Web/Cloud, and identifying failure points.	Ability to diagnose if an issue is network, device, or system-related.
Supp-02: User & Device Management	Managing user roles/permissions (RBAC), resetting passwords, registering/blocking POS terminals.	Effective administration of system users and devices.
Supp-03: Issue Resolution & Escalation	Troubleshooting common user errors, reading audit logs, and protocols for escalating technical bugs to Hydrolife Tech.	Proficiency in resolving L1/L2 issues and managing support tickets.
Supp-04: Reporting & Data Integrity	Generating ad-hoc reports for management, verifying transaction statuses, and identifying data discrepancies.	Supporting management with accurate data and verifying system integrity.

4. Change Management Strategy

To address "User Resistance" (identified in our Risk Management Strategy), we will implement the following:

1. **Change Champions:** Identify and train influential staff members in each department to act as peer mentors and advocates for the new system.
2. **Communication Campaign:** Regular updates, town halls, and internal memos explaining

the benefits of the system (e.g., "Easier work, not less work").

3. **Feedback Loop:** Establishing a clear channel for staff to report "pain points" during UAT (Week 7), ensuring their concerns are addressed before Go-Live.

5. Training Resources and Deliverables

Hydrolife Tech will provide the following materials as part of the engagement:

- **User Manuals:** Step-by-step guides with screenshots for all operational modules (PDF and Physical Copies).
- **Integrated Help Facility:** A "Help" button within the RAS web portal and Mobile App linking to FAQs and tutorials.
- **Video Tutorials:** Short, pre-recorded walkthroughs of key tasks (e.g., "How to print a parking receipt") accessible via the app.

6. Intensive 2-Week Knowledge Transfer Schedule (Project Weeks 7 & 8)


Phase	Activity	Timeline (Project Week)	Logistics Provided
Phase 1: Preparation	Needs Assessment & Training Material Finalization	Prior to Week 7	Training Manuals
Phase 2: Operational Training	Revenue Staff, Cashiers & Change Champions Training	Week 7 (5 Days Intensive)	Venue, Materials, POS Units, Test Environment
Phase 3: Executive & Technical Handover	Executive Workshops (Strategic Track) & ICT Support Handover	Week 8 (5 Days Intensive)	Venue, Refreshments, Cloud Access Credentials
Phase 4: Post-Deployment Support	On-the-job Support & Issue Escalation (Retention Period)	Month 1-2 (Post Go-Live)	On-site Support Staff

7. Evaluation and Certification

- **Competency Tests:** Revenue collectors will undergo a practical test on POS usage. Only

those achieving a pass mark will be issued login credentials for the live system.

- **Certification:** Certificates of Completion will be awarded to all trainees who successfully complete the course.
- **Feedback Forms:** Participants will evaluate the training quality to allow us to refine the approach for the post-implementation support phase.

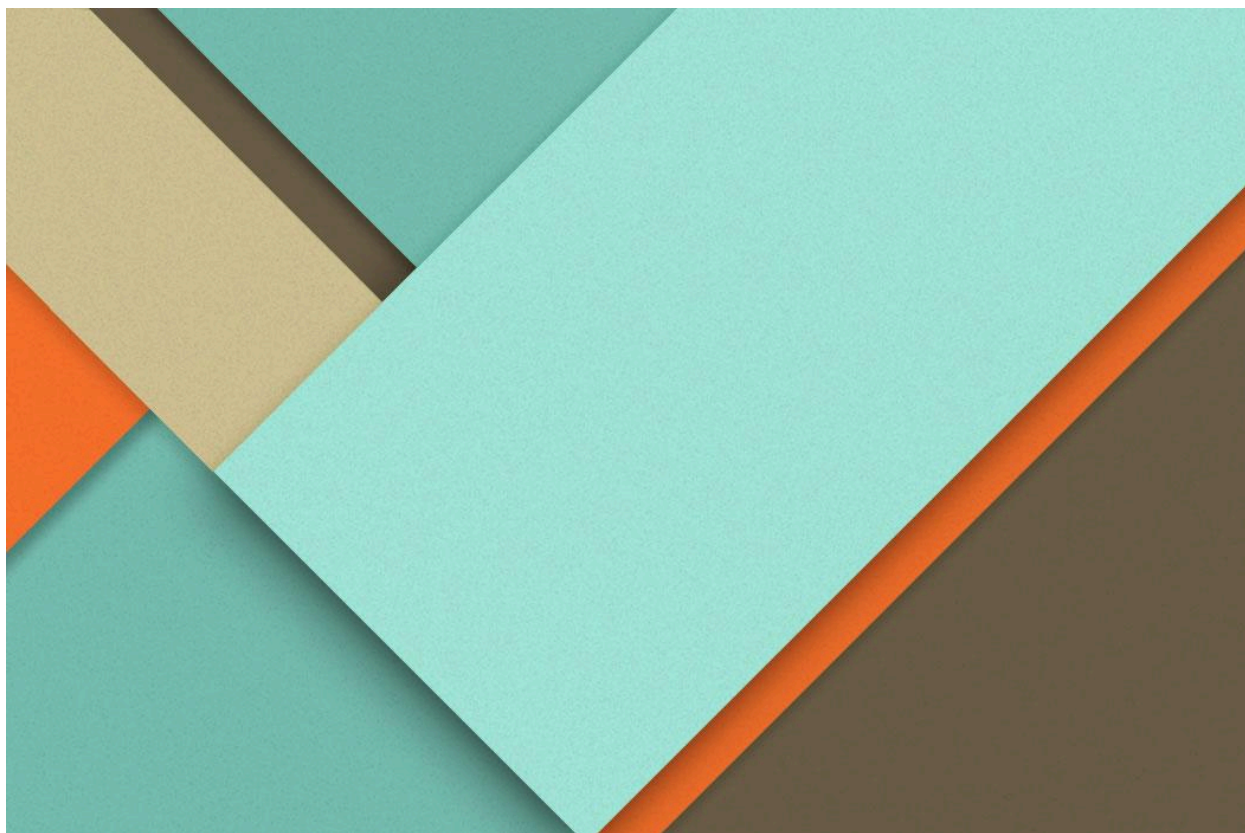

STAFF CERTIFICATES





KABARAK UNIVERSITY

This is to certify that

Ngugi Calvin Njuguna

upon satisfying all the requirements, and on the
recommendation of Senate, is hereby conferred the degree of


**Bachelor of Science in Information
Technology
Second Class Honours (Lower Division)**

with all the honours, rights and privileges appertaining to this
degree at the Seventeenth Congregation held at this University on
the Seventeenth Day of December Two Thousand and Twenty One



Vice Chancellor





Deputy Vice Chancellor
(Academic and Research)



BScIT 2021/0000068



Certificate No 007339



Multimedia University of Kenya

This is to certify that

Chege Danche Ng'ang'a

having satisfied all the requirements for the
conferment of the degree of

**Bachelor of Science in Applied
Physics and Computer Science**



Second Class Honours - (Upper Division)

was admitted to the degree at a congregation
held at this University
on the Seventeenth Day of December in the
Year Two Thousand and Twenty One


Vice Chancellor




Deputy Vice Chancellor
(Academic Affairs)



SOUTH EASTERN KENYA UNIVERSITY

This is to certify that

Mutisya Joel Ngite

having satisfied the requirements
for the award of the degree of the

Bachelor of Information Technology

Second Class Honours (Upper Division)

was admitted to the degree
at a Congregation held at
this University on the

Thirty First Day of October in the Year
Two Thousand and Twenty Four



VICE-CHANCELLOR

DEPUTY VICE-CHANCELLOR
(ACADEMIC, RESEARCH AND INNOVATION)

REGISTRAR
(ACADEMIC REGISTRAR)

20 1473



Maseko University

*On the recommendation of the University Senate
and by virtue of the authority vested in the University, hereby confer upon*

Ong'any Onyango Mathews

the degree of


Bachelor of Science (Information and Communication Technology Management)

Second Class Honours (Lower Division)

*In testimony thereof this award was conferred at the congregation held at this University on
Friday the 30th April, 2021*

Vice-Chancellor

*Deputy Vice-Chancellor,
Academic & Student Affairs*

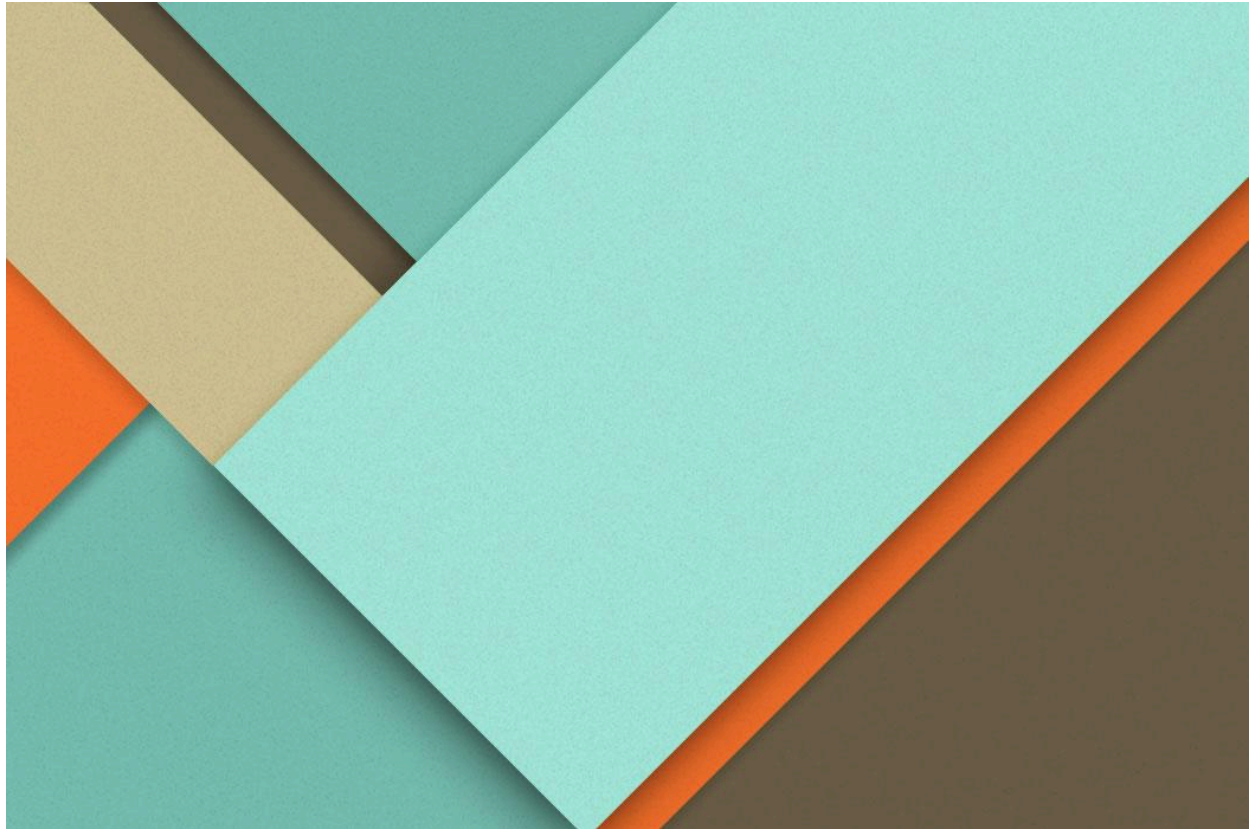

COMPANY REFERENCES





PURCHASE ORDER

P.O BOX 34 – 60300 Isiolo.
0790663616

PO #: HS2012532
DATE: 17-05-2023

VENDOR INFORMATION

Hydrolife Tech Limited
P.O BOX 37647 - 00100
Nairobi.
Phone: 0794164351

Ordered by:

Duba Aloiw

Position

Chief Procurement Officer




ID	ITEM DESCRIPTION	QTY	UNIT PRICE	TOTAL
1	Warehouse Management Software Design, development, and deployment of a custom-built Warehouse Management Software tailored to client operations, including system integration, user training, and technical support.	1	Ksh 12,850,000	Ksh 12,850,000

Chief Procurement Officer

DUBA ALIOW 

General Manager

ALI HUSSEIN 

ANDALUSI CONTRACTORS
AND SUPPLIERS LTD
P.O. Box 34-60300
ISIOLO

SUBTOTAL Ksh 12,850,000

TAX RATE 16%

GRAND TOTAL:

Ksh 14,906,000



PURCHASE ORDER

Bill To:
Kivulini Trust
P.O BOX 381 - 000242
Kitengela
0720362381

Ship to:
Kivulini Trust
P.O BOX 381 - 000242
Kitengela
0720362381

PURCHASE ORDER #
000859

ORDER DATE
10/02/2025

Performed By:
Hydrolife Tech Limited
P.O. Box 37646 – 00100
Nairobi.
0794164351

N
Phone: [Insert Contact Number]
Email: [Insert Company Email]

Qty	Description				Unit Price	Line Total
1	Provision of Archeological & Cultural Mapping System				Ksh 7,000,000	Ksh 7,000,000

SUBTOTAL: Ksh 7,000,000
VAT (16%): Ksh 1,120,000
TOTAL: Ksh 8,120,000

Shipping Date: 17/04/2025

Accepted By:

Date:

Approved By:





AL SHAMIM OVERSEAS LIMITED

P.O. BOX 8935-00200 NAIROBI, KENYA
KAMPALA ROAD- INDUSTRIAL AREA
alshamim@gmail.com | +254721021031

Purchase Order

AOL/PO/27/2023


Date: 2nd -Aug-2023

Supplier: M/S HYDROLIFE TECH LIMITED P.O BOX 37646-00100, NAIROBI.			Ship To: Head Office Nairobi		
Item	Description	Unit/Qty	Unit Price	Amount	Completion Date
OST071	SUPPLY, INSTALLATION, TESTING AND COMMISSIONING OF WAREHOUSE MANAGEMENT SYSTEM	Lot Scope: • Supply, Installation, Testing and Commissioning of Warehouse Management Systems. • User training • Integration testing • Commissioning	6,672,493.89	6,672,493.89	90 Working Days


AL SHAMIM OVERSEAS LIMITED
P.O. BOX 10902-00400,
NAIROBI

SUB TOTAL KES *** 6,672,493.89
VAT TOTAL KES *** INCLUSIVE
TOTAL KES *** 6,672,493.89

Prepared By: 

Approved By: 

Please deliver the above Goods/Services under the Terms and Conditions stated. Validity 30Days

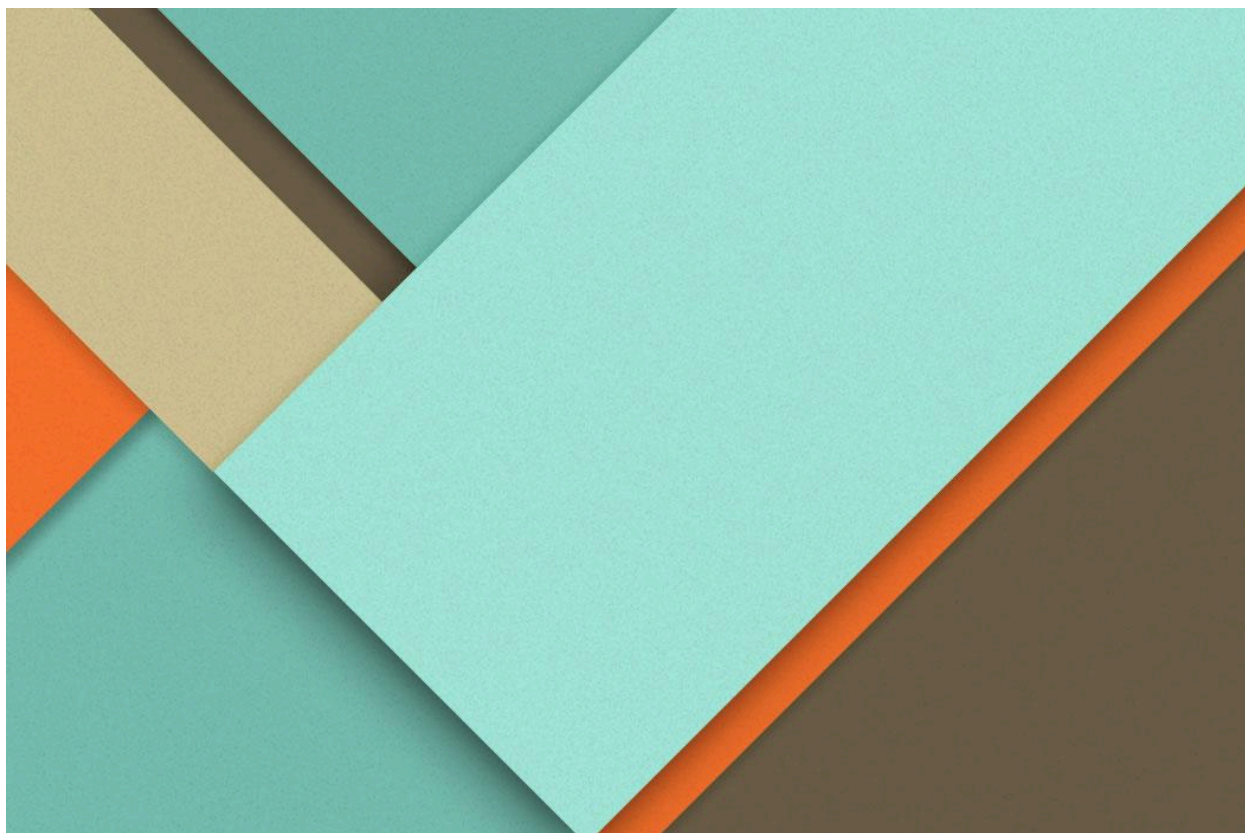

FINANCIAL PROPOSAL





**REPUBLIC OF KENYA
COUNTY GOVERNMENT OF ISIOLO
DEPARTMENT OF REVENUE**



FINANCIAL PROPOSAL

**REVENUE AUTOMATION SYSTEM FOR COUNTY GOVERNMENT OF
ISIOLO**

TENDER NO: CGI/RFP/ FEP/01/2025-2026

SUBMITTED BY:

HYDROLIFE TECH LIMITED

9TH FLOOR, CIANDA HOUSE, NAIROBI

P.O. BOX 37646 - 00100,

NAIROBI-KENYA.

TEL: 0731206395

EMAIL: info@hydrolifetech.com

NOV, 2025

FINANCIAL PROPOSAL

REVENUE AUTOMATION SYSTEM FOR COUNTY GOVERNMENT OF ISIOLO

Tender No: CGI/RFP/FEP/01/2025-2026

SUBMITTED TO:

The Chief Officer Revenue

County Government of Isiolo

P.O. Box 36-60300, Isiolo

SUBMITTED BY:

Hydrolife Tech Limited

P.O Box 37646 - 00100, Nairobi.

Address: 9th Floor, Cianda House, Nairobi

Authorized Representative: Kulah Jirma, Director

Email: info@hydrolifetech.com

Date: November 24, 2025

FORM F-1: FINANCIAL PROPOSAL SUBMISSION FORM

Date: 24th Nov 2025

To: The Chief Officer Revenue

County Government of Isiolo

P.O. Box 36 - 60300 ISIOLO

Ladies/Gentlemen:

We, the undersigned, offer to provide the consulting services for **DEVELOPMENT OF REVENUE AUTOMATION SYSTEM FOR COUNTY GOVERNMENT OF ISIOLO** in accordance with your Request for Proposal **Tender No:** CGI/RFP/FEP/01/2025-2026 dated 12th Nov 2025 and our Proposal.

Our attached Financial Proposal is for the sum of **Kenya** Shillings Nineteen Million, **Nine**

Hundred and Eighty Thousand Only (Ksh 19,980,000). This amount is inclusive of the local taxes.

Our Financial Proposal shall be binding upon us subject to the modifications resulting from Contract negotiations, up to expiration of the validity period of the Proposal.

Commissions and gratuities paid or to be paid by us to agents relating to this Proposal and Contract execution, if we are awarded the Contract, are listed below:

None

We understand you are not bound to accept any Proposal you receive.

We remain,

Yours sincerely,

Kulah Jirma Director

Hydrolife Tech Limited

FORM F-2: SUMMARY OF COSTS

Item	Costs (Ksh)
A. Remuneration (Personnel Costs)	5,600,000
B. Reimbursable & Operational Costs	11,624,138
Sub-Total (Exclusive of Taxes)	17,224,138
C. Taxes (16% VAT)	2,755,862
TOTAL AMOUNT OF FINANCIAL PROPOSAL	19,980,000

FORM F-3: BREAKDOWN OF REMUNERATION PER ACTIVITY

Based on an 8-Week (2 Month) Project Duration for Key Personnel.

Name	Position	Staff-Months	Monthly Rate (Ksh)	Total Amount (Ksh)
Key Personnel				
Mathews Onyango	Project Manager	2.0	800,000	1,600,000
Chege Danche	Lead System Analyst / DevOps	2.0	800,000	1,600,000
Calvin Njuguna	Lead Software Engineer	2.0	700,000	1,400,000
Joel Mutisya	Implementation & Training Lead	2.0	500,000	1,000,000
Sub-Total Remuneration				5,600,000

FORM F-4: BREAKDOWN OF REIMBURSABLE & OPERATIONAL COSTS

Detailed breakdown of infrastructure, hardware, training, and deployment costs necessary for the 8-week delivery.

No.	Description	Unit	Quantity	Unit Cost (Ksh)	Total Amount (Ksh)
1.0	Cloud Infrastruct				

	ure & Licensing				
1.1	AWS Cloud Hosting & Storage Credits (12 Months Prepaid)	Lumpsum	1	2,000,000	2,000,000
1.2	SSL Certificates & Domain Security (Wildcard)	Years	2	150,000	300,000
1.3	Third-Party API Aggregator Fees (SMS/Payments Setup)	Lumpsum	1	500,000	500,000
2.0	Hardware & Equipment Supply				
2.1	Android POS Terminals (Ruggedized with Printer) for Collectors	Units	50	45,000	2,250,000
2.2	Biometric/Security Devices for Server Access	Set	1	450,000	450,000
3.0	Training &				


	Capacity Building				
3.1	Executive Stakeholder Workshops (Venue, Logistics)	Days	3	250,000	750,000
3.2	Revenue Staff Training Sessions (Venue, Refreshments, Materials)	Days	5	300,000	1,500,000
3.3	Technical Admin Training (Cloud & DevOps Handover)	Days	5	100,000	500,000
4.0	Implementation & Go-Live				
4.1	Data Migration & Cleaning (Legacy Records)	Lumpsum	1	1,200,000	1,200,000
4.2	Security Audit & Penetration Testing (Third-Party Certification)	Lumpsum	1	800,000	800,000

4.3	Go-Live Launch & Change Management Publicity	Lumpsum	1	500,000	500,000
5.0	Contingency				
5.1	Miscellaneous / Contingency (5% of Subtotal)	Sum	1	874,138	874,138
	Total Reimbursables				11,624,138

FORM F-5: PAYMENT SCHEDULE

Aligned with the Terms of Reference Milestones.

Milestone	Deliverable	Percentage	Amount (Ksh)
1. Inception	Submission of Inception Report (Week 1)	10%	1,998,000
2. Interim	Submission of Interim Report (Week 5)	25%	4,995,000
3. Draft Final	Submission of Draft Final Report (		

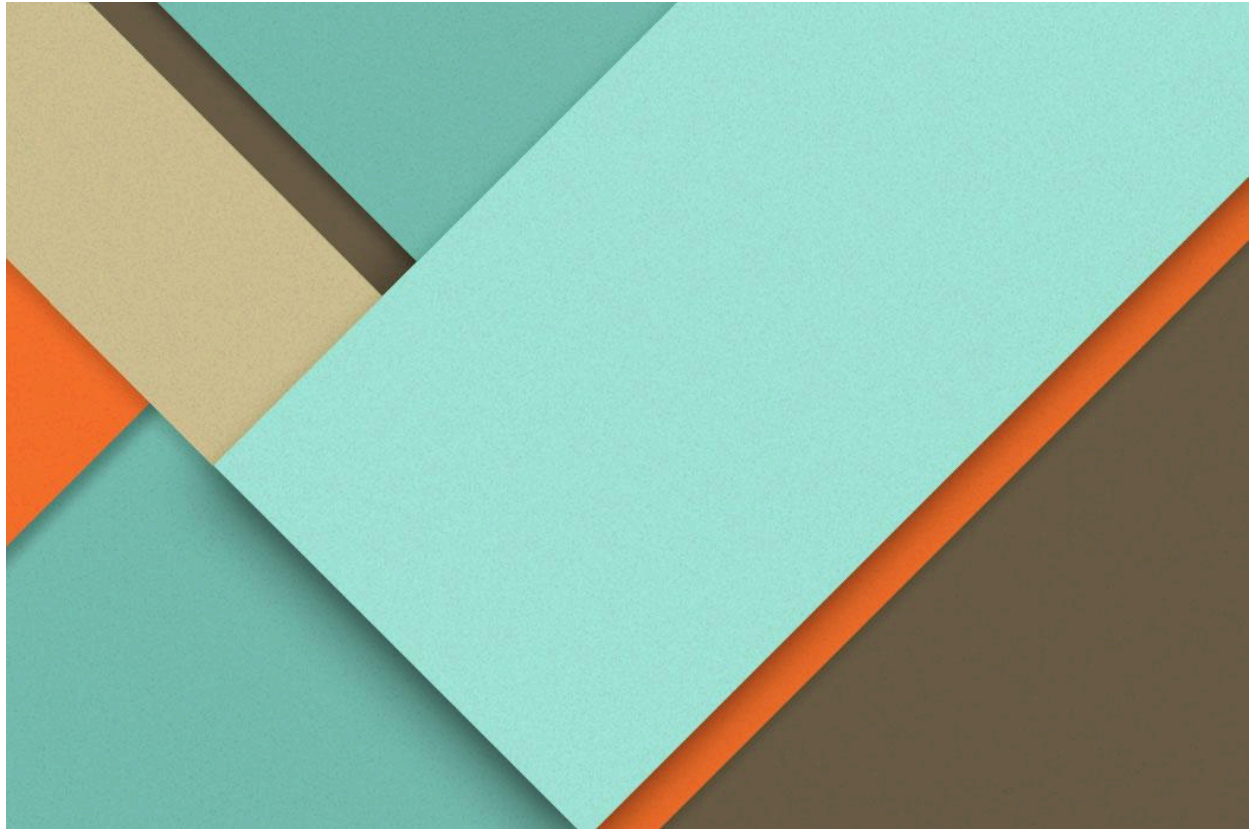

STATUTORY DOCUMENTS



OUR REF: CC-EP919ARE

22nd October
2025

KULAH ABDIKADIR JIRMA

**P.o Box 37646, 00100 - G.P.O
NAIROBI**

KAYJIRMA@GMAIL.COM

Dear Sir/Madam,

RE: HYDROLIFE TECH LIMITED CPR/2013/121666

We wish to inform you that your application for certified copies has been successfully processed. You may verify the documents on the BRS platform through scanning the QR code below. Please note that this document is password protected.



JOSHUA NYANG'ACHA

FOR: REGISTRAR OF COMPANIES

Disclaimer:

These certified copies contain personally identifiable information (PII) disclosed by the Business Registration Service (BRS) in compliance with its statutory obligations under the Companies Act and in the exercise of its official authority. This information is provided solely for the purpose for which it was requested. Any further processing, use, or disclosure that is incompatible with the original purpose is prohibited and may constitute a breach of the Data Protection Act, 2019.





No. CPR/2013/121666

CERTIFICATE OF INCORPORATION

I hereby CERTIFY, that -

HYDROLIFE TECH LIMITED

is this day Incorporated under the Companies Act(Cap.486) and that the Company is **LIMITED**.

GIVEN under my hand at Nairobi this **5 th** day of **November**
Two Thousand and **Thirteen**

Registrar Of Companies

Certificate Date : 12/07/2016

Personal Identification Number

P0514434980

This is to certify that taxpayer shown herein has been registered with Kenya Revenue Authority

Taxpayer Information

Taxpayer Name	HYDROLIFE TECH LIMITED
Email Address	HYDROLIFETECH@GMAIL.COM

Registered Address

L.R. Number :	Building : Hamilton House
Street/Road : Kaunda Street	City/Town : Nairobi
County : Nairobi	District : Starehe District
Tax Area : CBD	Station : Machakos*
P. O. Box : 37646	Postal Code : 00100

Tax Obligation(s) Registration Details

Sr. No.	Tax Obligation(s)	Effective From Date	Effective Till Date	Status
1	Value Added Tax (VAT)	05/11/2013	N.A.	Cancelled
2	Income Tax - Company	05/11/2013	N.A.	Active

Electronic Tax Invoicing Status

eTims Registration: Inactive	Tims Registration: Inactive
-------------------------------------	------------------------------------

The above PIN must appear on all your tax invoices and correspondences with Kenya Revenue Authority. Your accounting end month is December unless a change has been approved by the Commissioner-Domestic Taxes Department. The status of Tax Obligation(s) with 'Dormant' status will automatically change to 'Active' on date mentioned in "Effective Till Date" or any transaction done during the period. This certificate shall remain in force till further updated.

* The station is subject to change based on the verification done by Commissioner.

www.kra.go.ke**Taxpayer PIN :** P0514434980**Certificate Date:** 28/07/2025**Name and Address :****Hydrolife Tech Limited**Hamilton House, Nairobi, Starehe District,
PO Box:37646,
Postal Code:00100**Certificate Number:**

KRAMCS1511360325



**This is to confirm that Hydrolife Tech Limited,
Personal Identification Number P0514434980
has filed relevant tax returns and
paid taxes due as provided by Law.**

**This Certificate will be valid for
twelve (12) months up to 27/07/2026.**

Caveat: This certificate is issued on the basis of information available with the authority as at the certificate date mentioned above. The Authority reserves the right to withdraw the certificate if new evidence materially alters the tax compliance status of the recipient.

Disclaimer : This certificate is system Generated and therefore does not require signature. You may confirm validity of this certificate on the iTax Portal by using the TCC Checker. This certificate confirms your compliance status for a period of five years preceding the date of issue. The certificate may however be withdrawn on grounds of outstanding debt affecting periods prior to this.



NAIROBI CITY COUNTY

City Hall Building,
City Hall Way,
Nairobi, Kenya

P.O. Box 30075-00100
Nairobi, Kenya
info@nairobi.go.ke

UNIFIED BUSINESS PERMIT

TRADE LICENCE

LICENSE NO.: **UBP224683**
VALIDITY: **ANNUAL**

EFFECTIVE DATE: **07 NOV, 2025**
EXPIRY DATE: **06 NOV, 2026**

Nairobi City County grants this Trade License to

BUSINESS NAME: **HYDROLFE TECH LIMITED - -**

Registration details:

Registration No.: -

KRA PIN:

Postal address: **37646**

Physical address:

Unit: **914, Floor: 9, Cianda House,**
Plot: **209/638/2, Koinange Street, Nairobi**
Central, Starehe, Nairobi

To engage in the following activities/businesses/occupations:

600 PROFESSIONAL, TECHNICAL AND FINANCIAL SERVICES

Mini professional services firm with 1-5 employees/ professionals. Technicians guards etc.

- Computer Programming Activities

Having paid a license fee of **KES. 16,500.00 (SIXTEEN THOUSAND FIVE HUNDRED SHILLINGS ONLY)**

100	SBP	KES. 10,000.00
200	FIRE	KES. 6,000.00
400	PEST CONTROL	KES. 500.00

BUSINESS UNDER THIS PERMIT SHALL BE CONDUCTED AT THE ADDRESS AS INDICATED

DISCLAIMER

Issuance of this permit does not exempt the permit holder from compliance checks, inspections, top-ups or adherence to applicable laws. The Nairobi City County Trade Licensing Act 2019 Section 17(1) gives the Director the powers to suspend or cancel a permit in case of false information or non-compliance with the applicable laws.

Date of Issue: **07 Nov, 2025**

By Order of:



POWERED BY



UBP224683



Scan this QR Code to verify the authenticity of this document

Alternatively visit nairobiservices.go.ke

— Let's Make Nairobi Work —
www.nairobi.go.ke



NAIROBI CITY COUNTY

City Hall Building,
City Hall Way,
Nairobi, Kenya

P.O. Box 30075-00100
Nairobi, Kenya
info@nairobi.go.ke

TERMS & CONDITIONS

This licence is issued under section 12 of the Act subject to the following terms and conditions: -

1. Compliance with the provisions of the Nairobi City County Trade Licensing Act and any other legislation relevant to the trade.
2. This licence is not transferable.
3. Where a business is carried on in or from more than one premise, the business carried on in or from each premise is deemed to be separated business and as such a separate license is required;
4. The licence holder must notify the Director of any changes in the nature of trade, directorship or ownership of the business, location of business or cessation of trade.
5. The licence is a Nairobi City County Government property and must be displayed in a conspicuous place within the business premises and the licence holder must produce the licence whenever an authorized officer requires him or her.
6. The owner of the business should not sell/display their goods outside their licensed premises.
7. A person who forges or alters a licence without authority commits an offence and shall be liable on conviction to a fine not exceeding Kenya shillings fifty thousand or to imprisonment for a term not exceeding three months, or both.
8. A person who fails or neglects to renew a licence as required and continues to operate the business or trade commits an offence and shall be liable on conviction to a fine not exceeding Kenya shillings fifty thousand or to imprisonment for a term not exceeding three months, or both.
9. Granting of this License does not legitimise any illegal activity including occupation of a county road reserve or any prohibited area.
10. Under this license, it shall be the duty of every occupier, or owner or agent of a house, or other premise to clean or cause to be cleaned ten meters radius around his or her house or other premises or any area otherwise in his or her control
11. The licence holder shall ensure that appropriate safety measures are in place to mitigate fire and other hazards.
12. The licensed business shall only be conducted in full compliance with National and County health and safety laws and regulations.
13. The licensed business shall submit to periodic inspections for compliance with applicable standards, regulations and laws.
14. The licence holder shall comply with any other condition or directive as shall be necessary for purposes of health, hygiene and safety.
15. Subject to compliance to provided signage dimensions, siting & location requirements as per Outdoor Advertising & Signages policy (2015), NCG Advertising Act (2018) & PLUPA (2019).

POWERED BY





Certificate of Accreditation

This is to certify that:

HYDROLIFE TECH LIMITED (CPR/2013/121666)

Has demonstrated compliance with the Government IT Governance
Standard, Criteria for accreditation of Government ICT

Suppliers/Contractors and has been accredited under Category
ICTA 2: SYSTEMS AND APPLICATIONS for the provision of ICT services in the
scope of accreditation commencing from **06-11-2025** to **06-11-2026**

A blue ink signature, likely of the Chairman of the Accreditation Committee, consisting of a stylized, cursive script.

Chairman, Accreditation Committee

A blue ink signature, likely of the Director of Programmes and Standards, featuring a more complex, cursive script with a circular flourish at the end.

Director, Programmes and Standards



OFFICE OF THE
DATA PROTECTION
COMMISSIONER

Serial NO.: 15209

CERTIFICATE OF REGISTRATION



This certificate is awarded to
HYDROLIFE TECH LIMITED

Identification

807-3088-D53E as a

Data Controller

for a period of two (2) years starting from the date
indicated below.



Data Commissioner

Place of Issuance: Kenya. Certificate Valid from 06/10/2025 to 06/10/2027

*NOTE: This an online generated certificate





OFFICE OF THE
DATA PROTECTION
COMMISSIONER

Serial NO.: 15211

CERTIFICATE OF REGISTRATION



This certificate is awarded to
HYDROLIFE TECH LIMITED

Identification

807-3088-D53E as a

Data Processor

for a period of two (2) years starting from the date
indicated below.



Data Commissioner

Place of Issuance: Kenya. Certificate Valid from 06/10/2025 to 06/10/2027

*NOTE: This an online generated certificate

